
Sprint planning

Software Engineering 2 – Workshop #3

Agenda

- Overview of sprint planning ~30'
- Teams perform Sprint Planning ~2h
 - It's the work you will do in the next week
 - We'll go through teams to check your work

SPRINT PLANNING

PLAN

- PLAN, v.t. To bother about the best method of accomplishing an accidental result.

Bierce A. (1911), The Devil's Dictionary

Sprint planning

Plans are useless !

Sprint planning

Planning is essential !

Sprint

- The basic iteration in the Scrum approach
 - It defines the timebox where work is performed
- Produces a piece of working software to be demonstrated and reviewed at the end of the sprint
- Length
 - From 1 to 4 weeks long

Sprint Planning – Part 1

- **What** will we do?
 - Product owner proposes stories in priority order
 - Team members decide whether to commit
 - Team's velocity / Yesterday's weather
 - Must fit the team's time budget
 - Set of committed stories that go into the sprint backlog
 - Define tasks that detail the work the team will do

Sprint Planning – Part 2

- **How** will we do it?
 - Decompose stories into tasks
 - This may trigger renegotiation of stories
 - Recommended max effort per task:
 - max 3h/person
 - better 2h/person

Sprint Backlog

- List of stories
- Related tasks
- Estimation:
 - Task hours 
 - Task points
 - Task count

Sprint Planning – Part 1

Product Backlog

Sprint backlog

To do

In progress

Done

Story #3

Story #1

Story #28

Story #2

Story #4

Story #12


Story #7

Story #33


Story #34

Story #22


Sprint Planning – Part 1: WHAT

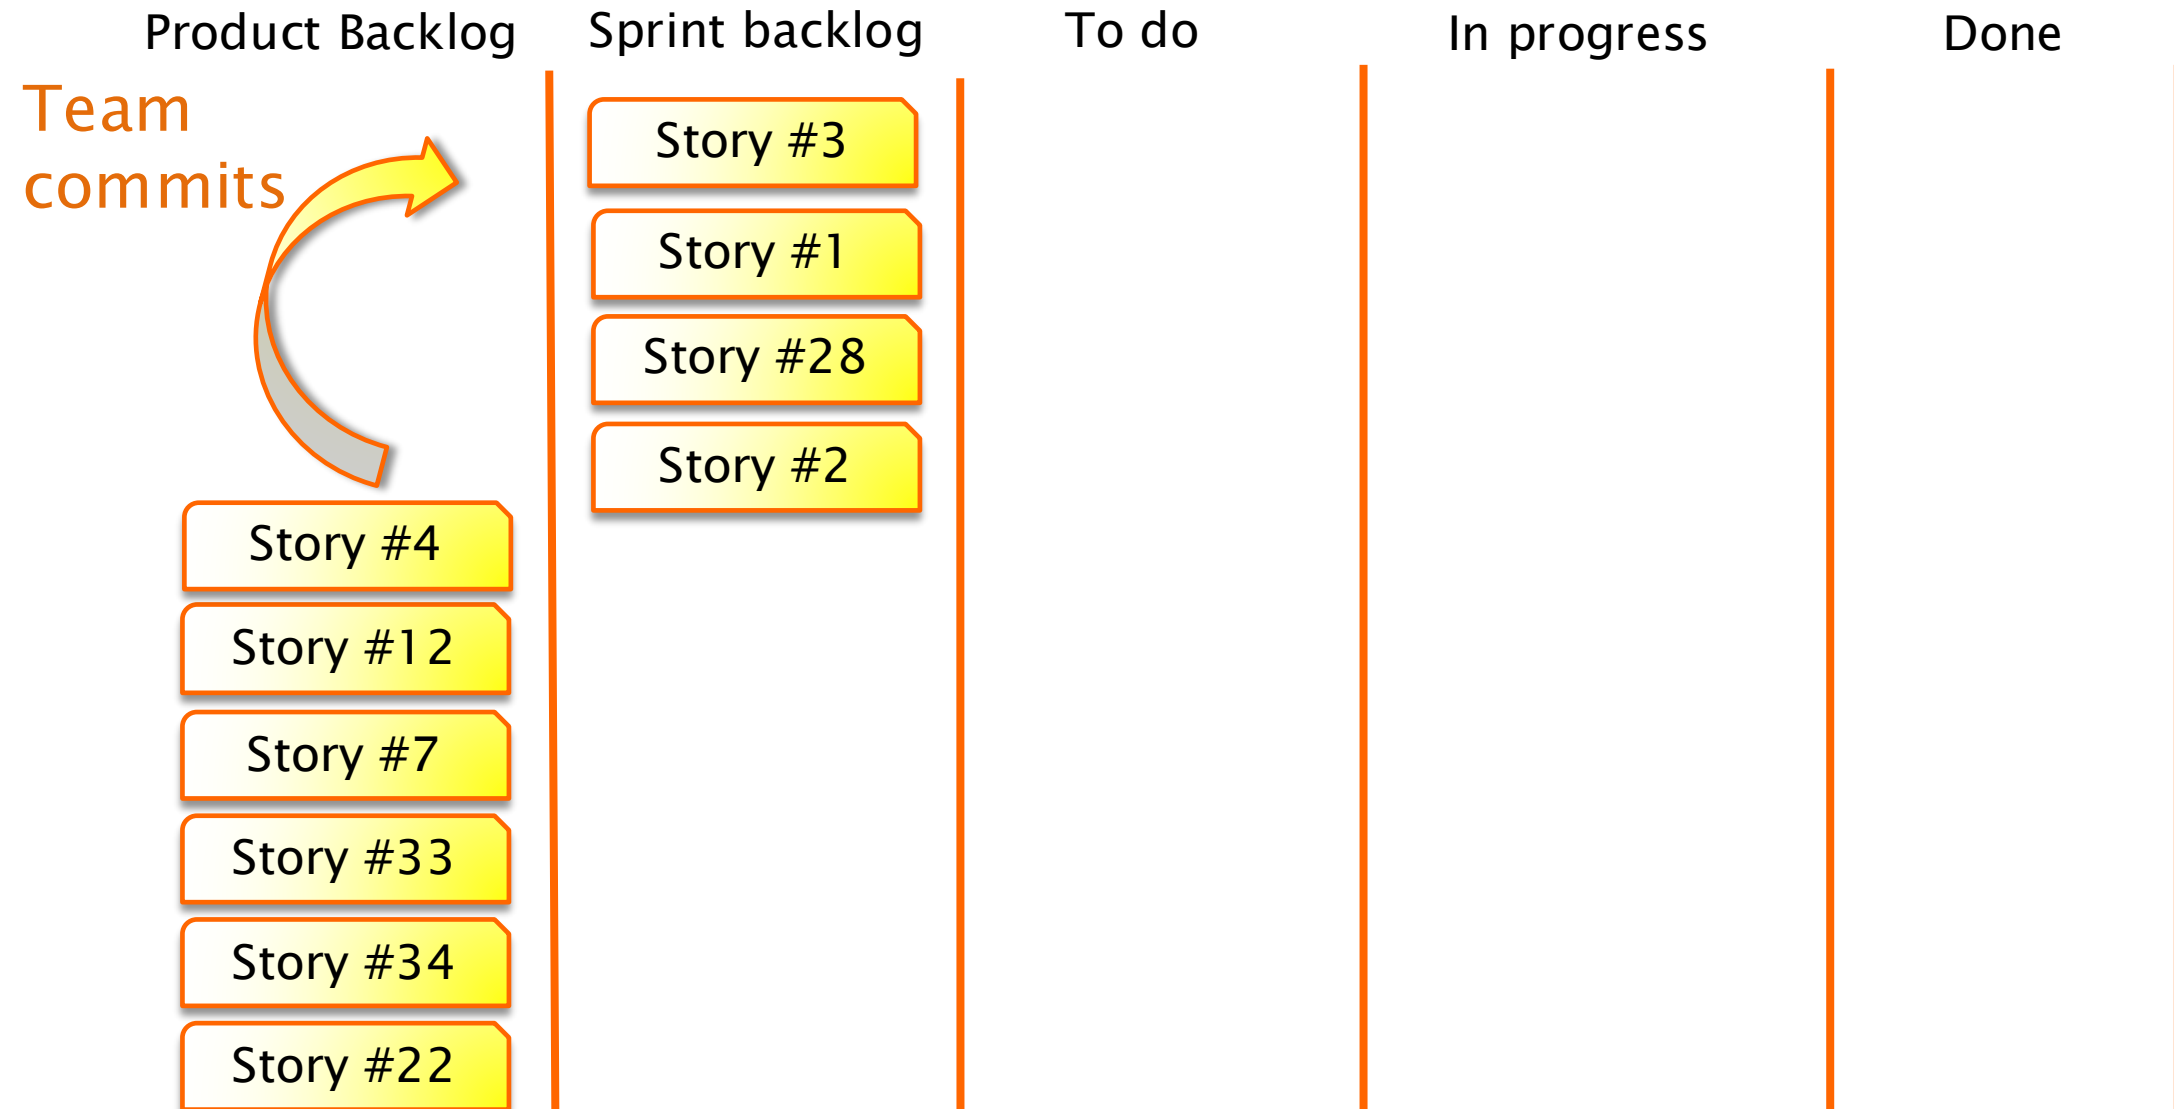

Sprint Planning – Part 2: HOW

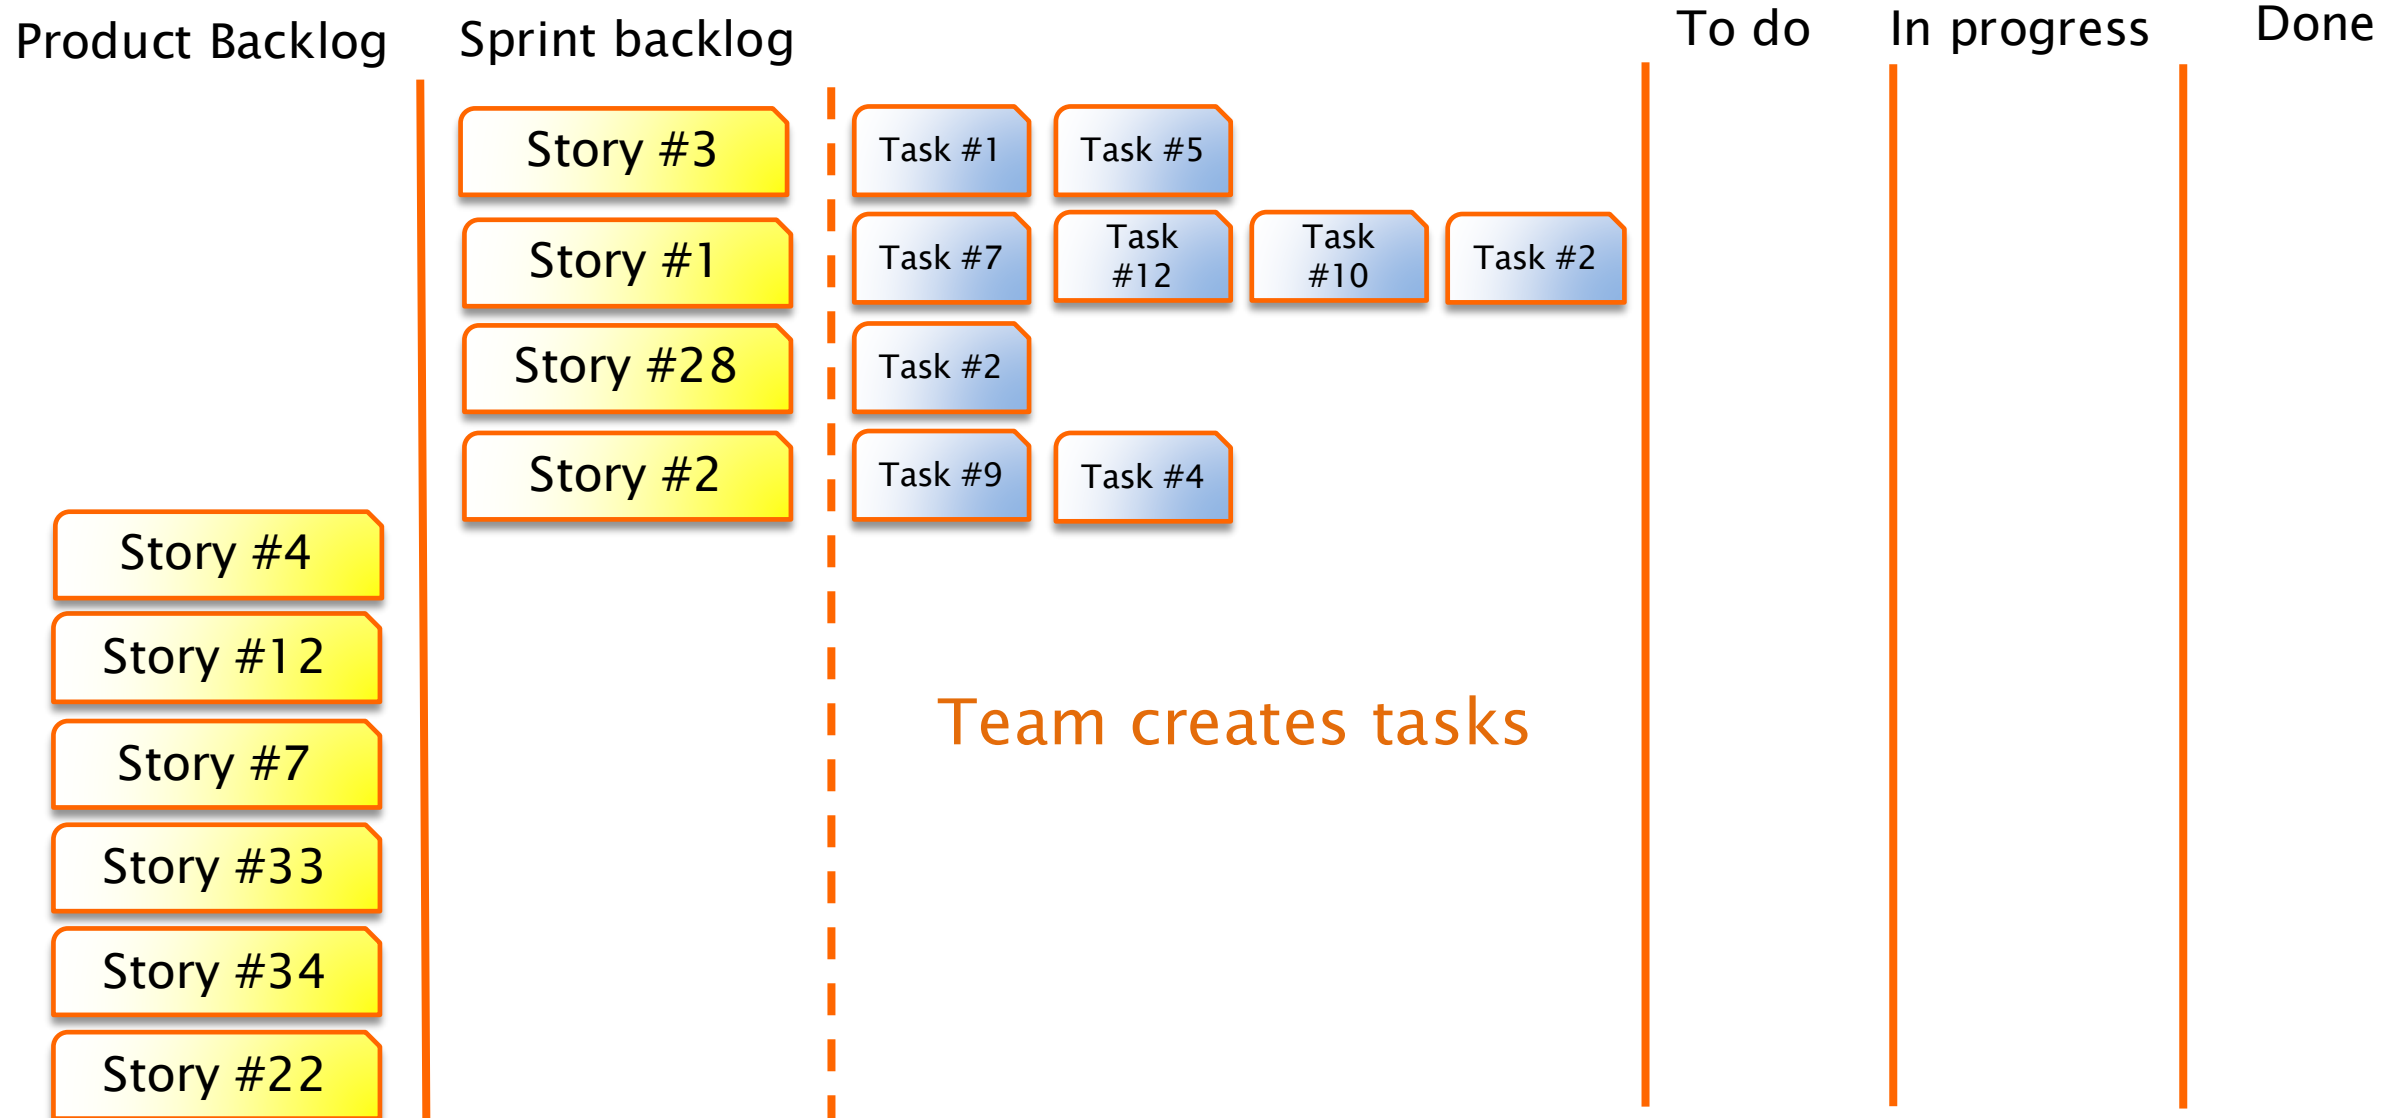

Sprint Goal

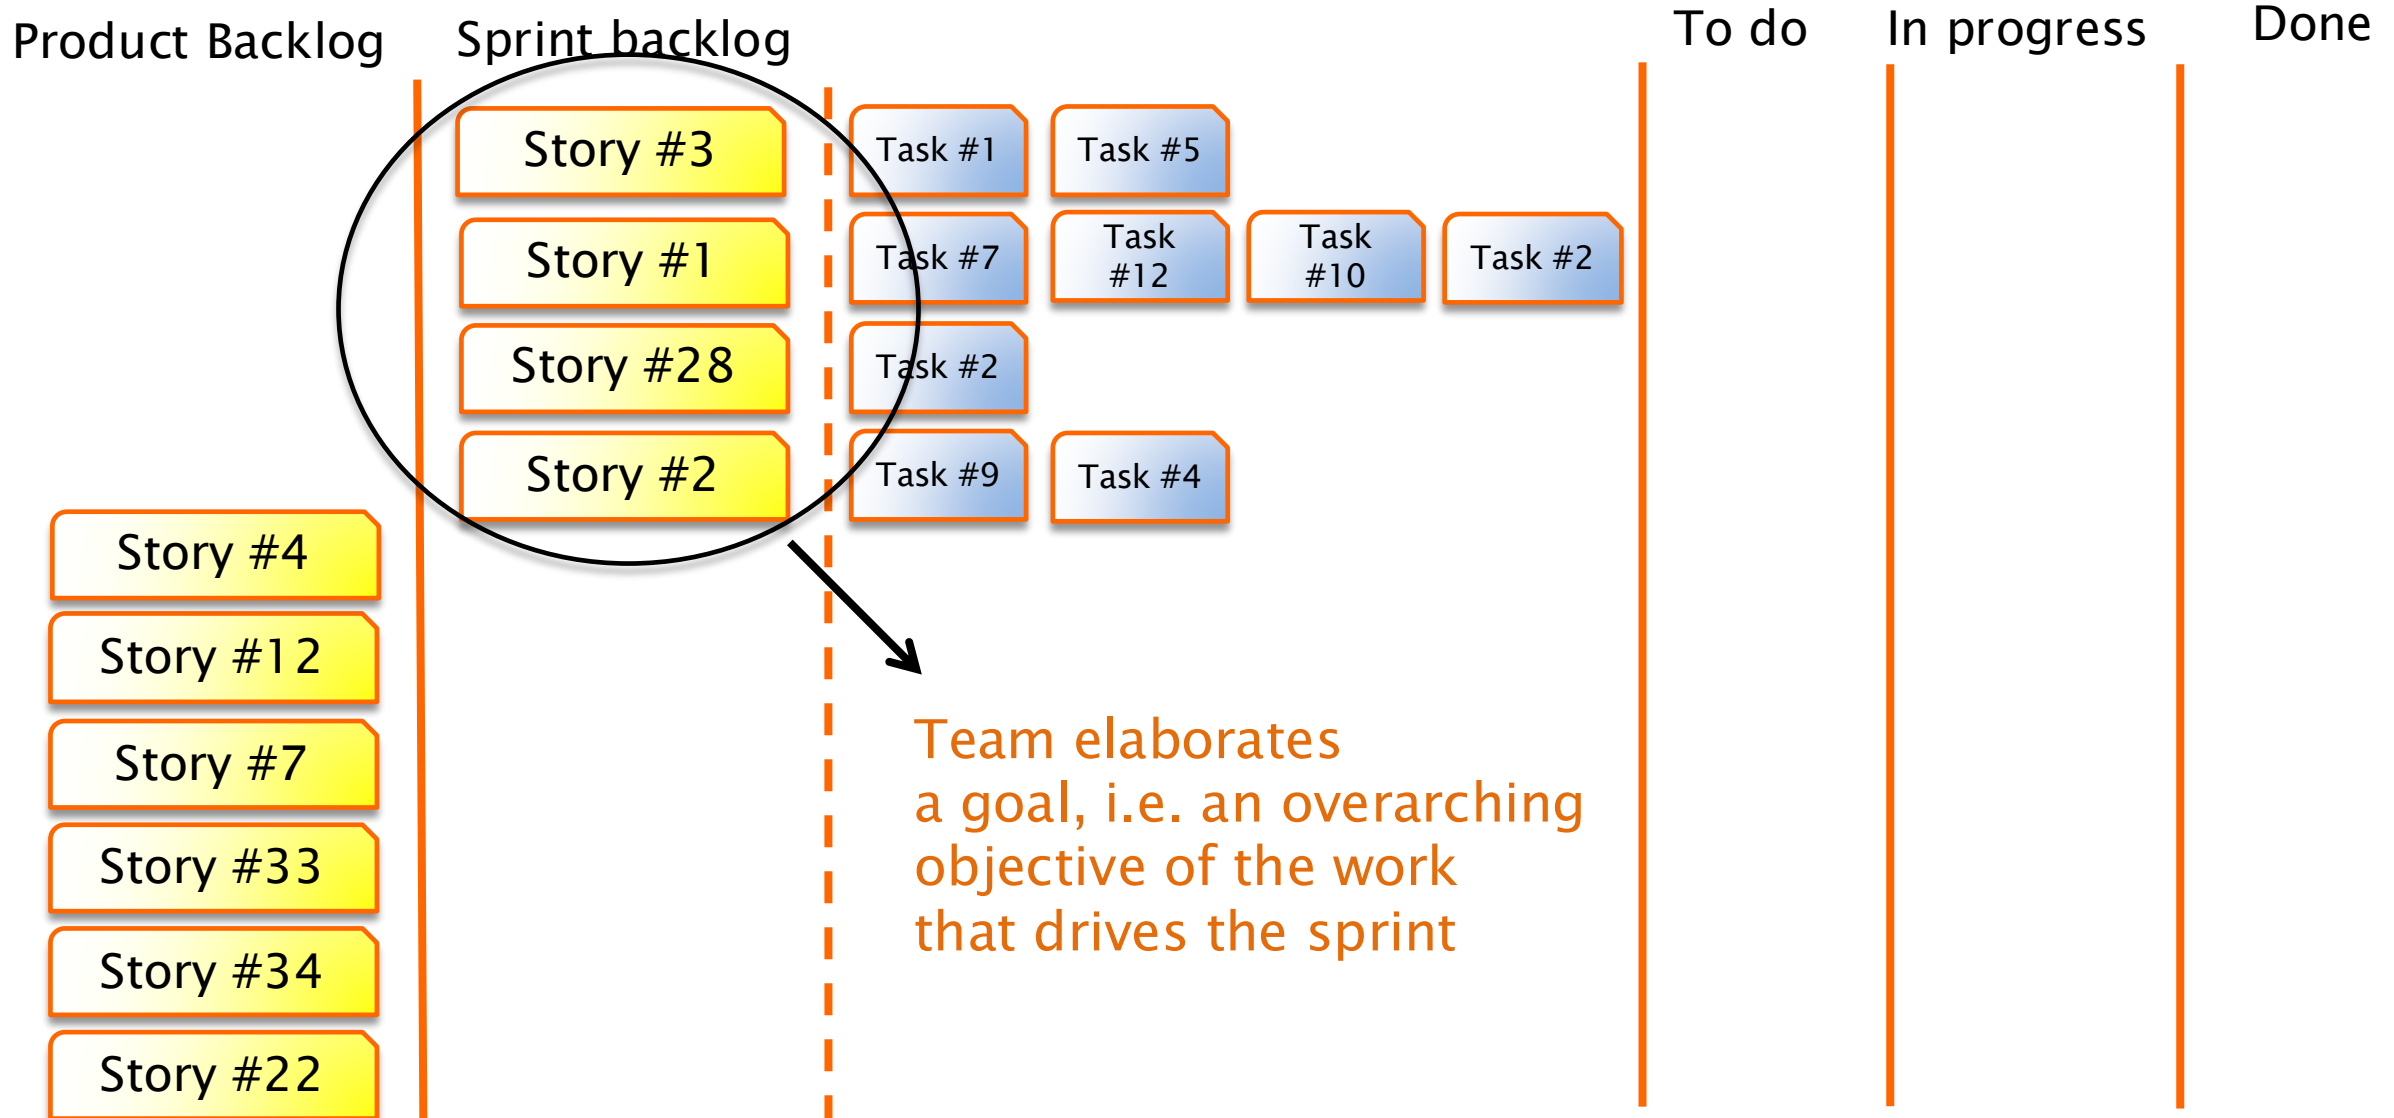

Task estimation

- Estimation is how much time the team is supposed to spend on it
 - Collectively: e.g., 2 persons working for 2 hours = 4 h
 - It might depend on who is going to perform the task
- The basis for estimation is the best knowledge you have at the time of planning

Assignment of tasks

- Work is never imposed !
- Every team member:
 - chooses their tasks
 - updates spent time as work proceeds
- Sprint backlog is emergent:
 - Tasks can be added, split, deleted, etc.
 - Sprint backlog is property of the team

Sprint progress

Sprint backlog

To do

In progress

To test/review

Done

Story #3

Story #1

Story #28

Story #2

Task #7

Task #9

Task #4

Task
#22

Task #5

Task
#12

Task
#20

Task #1

Task
#10

Task #2

Task #2

Task
#25

Example of assigned tasks and progress

Task (planned) ↓ / Time tracked →	Who	Mon	Tue	Wed	Thu	Fri
Create DB users and items (0,5h)	Marco		0,5			
Study Git documentation (2h)	Rebecca, Sofia	1 (R)	0,5 (R)		2 (S)	
Crate CSS for landing page (3h)	Sofia	1	0,5			
Review CSS (0,5h)	Giulio		0,5			
Design architecture (10h)	All	2 (all)				
Build test data on DB (4h)	Marco, Giulio			0,5 (M, G) 2 (G)		
Study popular ecommerce sites (8h)	Miriam		2	2	2	2

Definition of Done

An increment of product that is

*“thoroughly tested, well-structured, and well-written code that has been built into an executable and that the user operation of the functionality is documented, either in Help files or in user documentation.
This is the definition of a done increment.”*

Ken Schwaber. “Agile Project Management with Scrum”.

Base Definition of Done @SE2

- Unit tested
 - Integration and E2E tested
 - Code reviewed
 - Code pushed on Github
-
- You can try to enhance it in future sprints

PLANNING YOUR SPRINT

First sprint – Office Queue

- This sprint will last one week
 - Total effort budget: 8 hours per person
 - Add 2 hours for your work in class today
 - **TOTAL TIME TO PLAN : 10 h/person**
- Stories must be “done” (as in DoD)
- All work must be planned and tracked
 - Setup
 - Testing
 - Production code
 - Meetings (including sprint planning)

Performing Sprint Planning (1)

- Sprint planning is itself part of the sprint
 - You should add a Sprint Planning task to track time
- Process:
 - Select a story from product backlog
 - Divide it into tasks
 - Estimate and self-assign tasks
 - Repeat until budget is consumed
 - Review everything
 - Remember your time budget cap

Performing Sprint Planning (2)

- Only stories selected by the team for the sprint are divided into tasks
- You must respect the priority decided by the PO,
 - driven by value or other specific interests,
 - not complexity, effort, size, logical precedence, etc.
- You can add technical tasks, not directly related to a single story (e.g. setup application)

General comments on tasks (1)

- There might be relations between tasks
- Technical/crosscutting tasks may be standalone tasks not belonging to any story
- Discussing, understanding, and deciding about technology, is a task
 - Don't use too much of the sprint planning time for it
- Learning a new tool/technology/programming language, is a task

General comments on tasks (2)

- Task should be small to enable quick feedback cycles within the team
 - Keep them around 1h~2h/person
 - Exceptional cases up to 3h/person
 - For the collaborative group tasks, look at the duration
- If a team member is not confident with planned tasks, they should be proactive and propose others
 - Improve skills useful for the project
 - Review the artifacts done by other
 - ...

General comments on tasks (3)

- You shall track not only the estimate of the task, but also the actual time spent by each one on which task
- Otherwise, it will be impossible to:
 - Check plan vs ongoing work
 - Check whether your estimate was correct
 - Check whether you are working too much/too less
- Remember to enable time tracking in YouTrack!

SPRINT PLANNING IN YOUTRACK

PRACTICAL GUIDELINES FOR RUNNING THE SPRINT

Recommendations on sprint run (1)

- Only stories selected by the team for the sprint (and split into tasks) are developed during the sprint
- Your work time during the sprint is a fixed quantity: 8 hours per week per person (+2 in class)
- You should neither work much more, nor much less
 - 6 hours NOT OK
 - 10 hours NOT OK
 - 7,5 hours OK
 - 9 hours barely OK

Recommendations on sprint run (2)

- If you implemented all stories before the end of the sprint and you have time left:
 - You can add tasks devoted to improve quality of what you have done (more tests, more comments, etc.)
 - You can ask the PO if it is fine with them to add a new story in the sprint: remember to meet the DoD !

Recommendations on sprint run (3)

- Your goal for the end of the sprint is to have as many story **done** as possible:
 - Do not start tasks belonging to many stories in parallel, the risk is you will not have any of them done at the end
 - It is better to have one story done than three “*almost done*”

Recommendations on sprint run (4)

- As soon as you start a task you should change its state to “In Progress”
 - First of all: create a Sprint Planning task in the sprint and move it to progress
- You must track your time in YouTrack
 - As soon as you finish a working session

Recommendations on the dev. environment


- All relevant information concerning the organization and development of your work should be either on Youtrack or on Github
- For other types of information or artefact useful for coordination among team members, you can use other tools
 - If you deem those files relevant, mention them on a specific file on Github

Your sprint: 5–12 Oct.

- Starts... **NOW!**
 - Plan 2 hours per person today in classroom time
 - **TRACK THEM BEFORE YOU LEAVE !**
 - Plan 8 hours per person in the sprint
 - 10h between today 4pm and Monday 12 Oct. 4pm
- End of Sprint (Monday 12 Oct): Project Review
 - Demo of the software product
 - Feedback from stakeholders

Checklist Planning

- Only user stories selected for the sprint and split down into task in the current sprint board
- The total estimation of all tasks is $10h * n_members$
 - NB: $1d = 8h$ --> If you are 6, $60h = 7d 4h$
- There is a Sprint Planning task
 - In Uncategorized Cards
 - All team members assigned and estimation = $n * 2 h$
- All task should be in the Open column

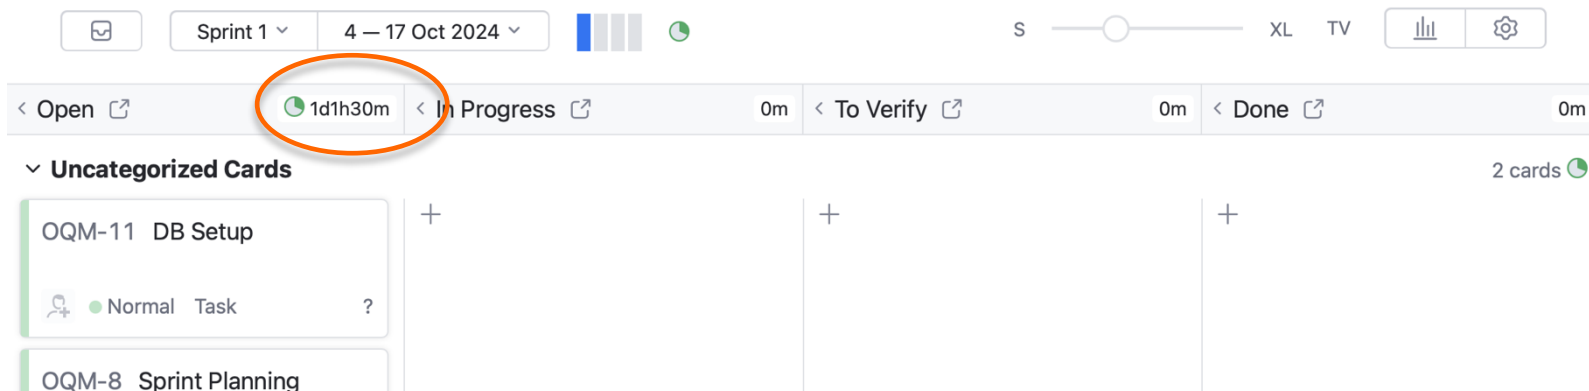

Setup the development infrastructure

- Complete planning on  **YouTrack**
 - All tasks estimated and possibly assigned
- Create a public  **GitHub** repository for your project

Write the link

- Add the GitHub links in the shared sheet
 - Before Friday 9 Oct. to avoid penalties



<https://vado.li/se2-oqm>

Presence



FAQ

- Do we have to think about a login?
 - A page where the user selects their role is enough
